


CARES ACT


K12 WIRELESS
IMPROVEMENTS

MEETING#6

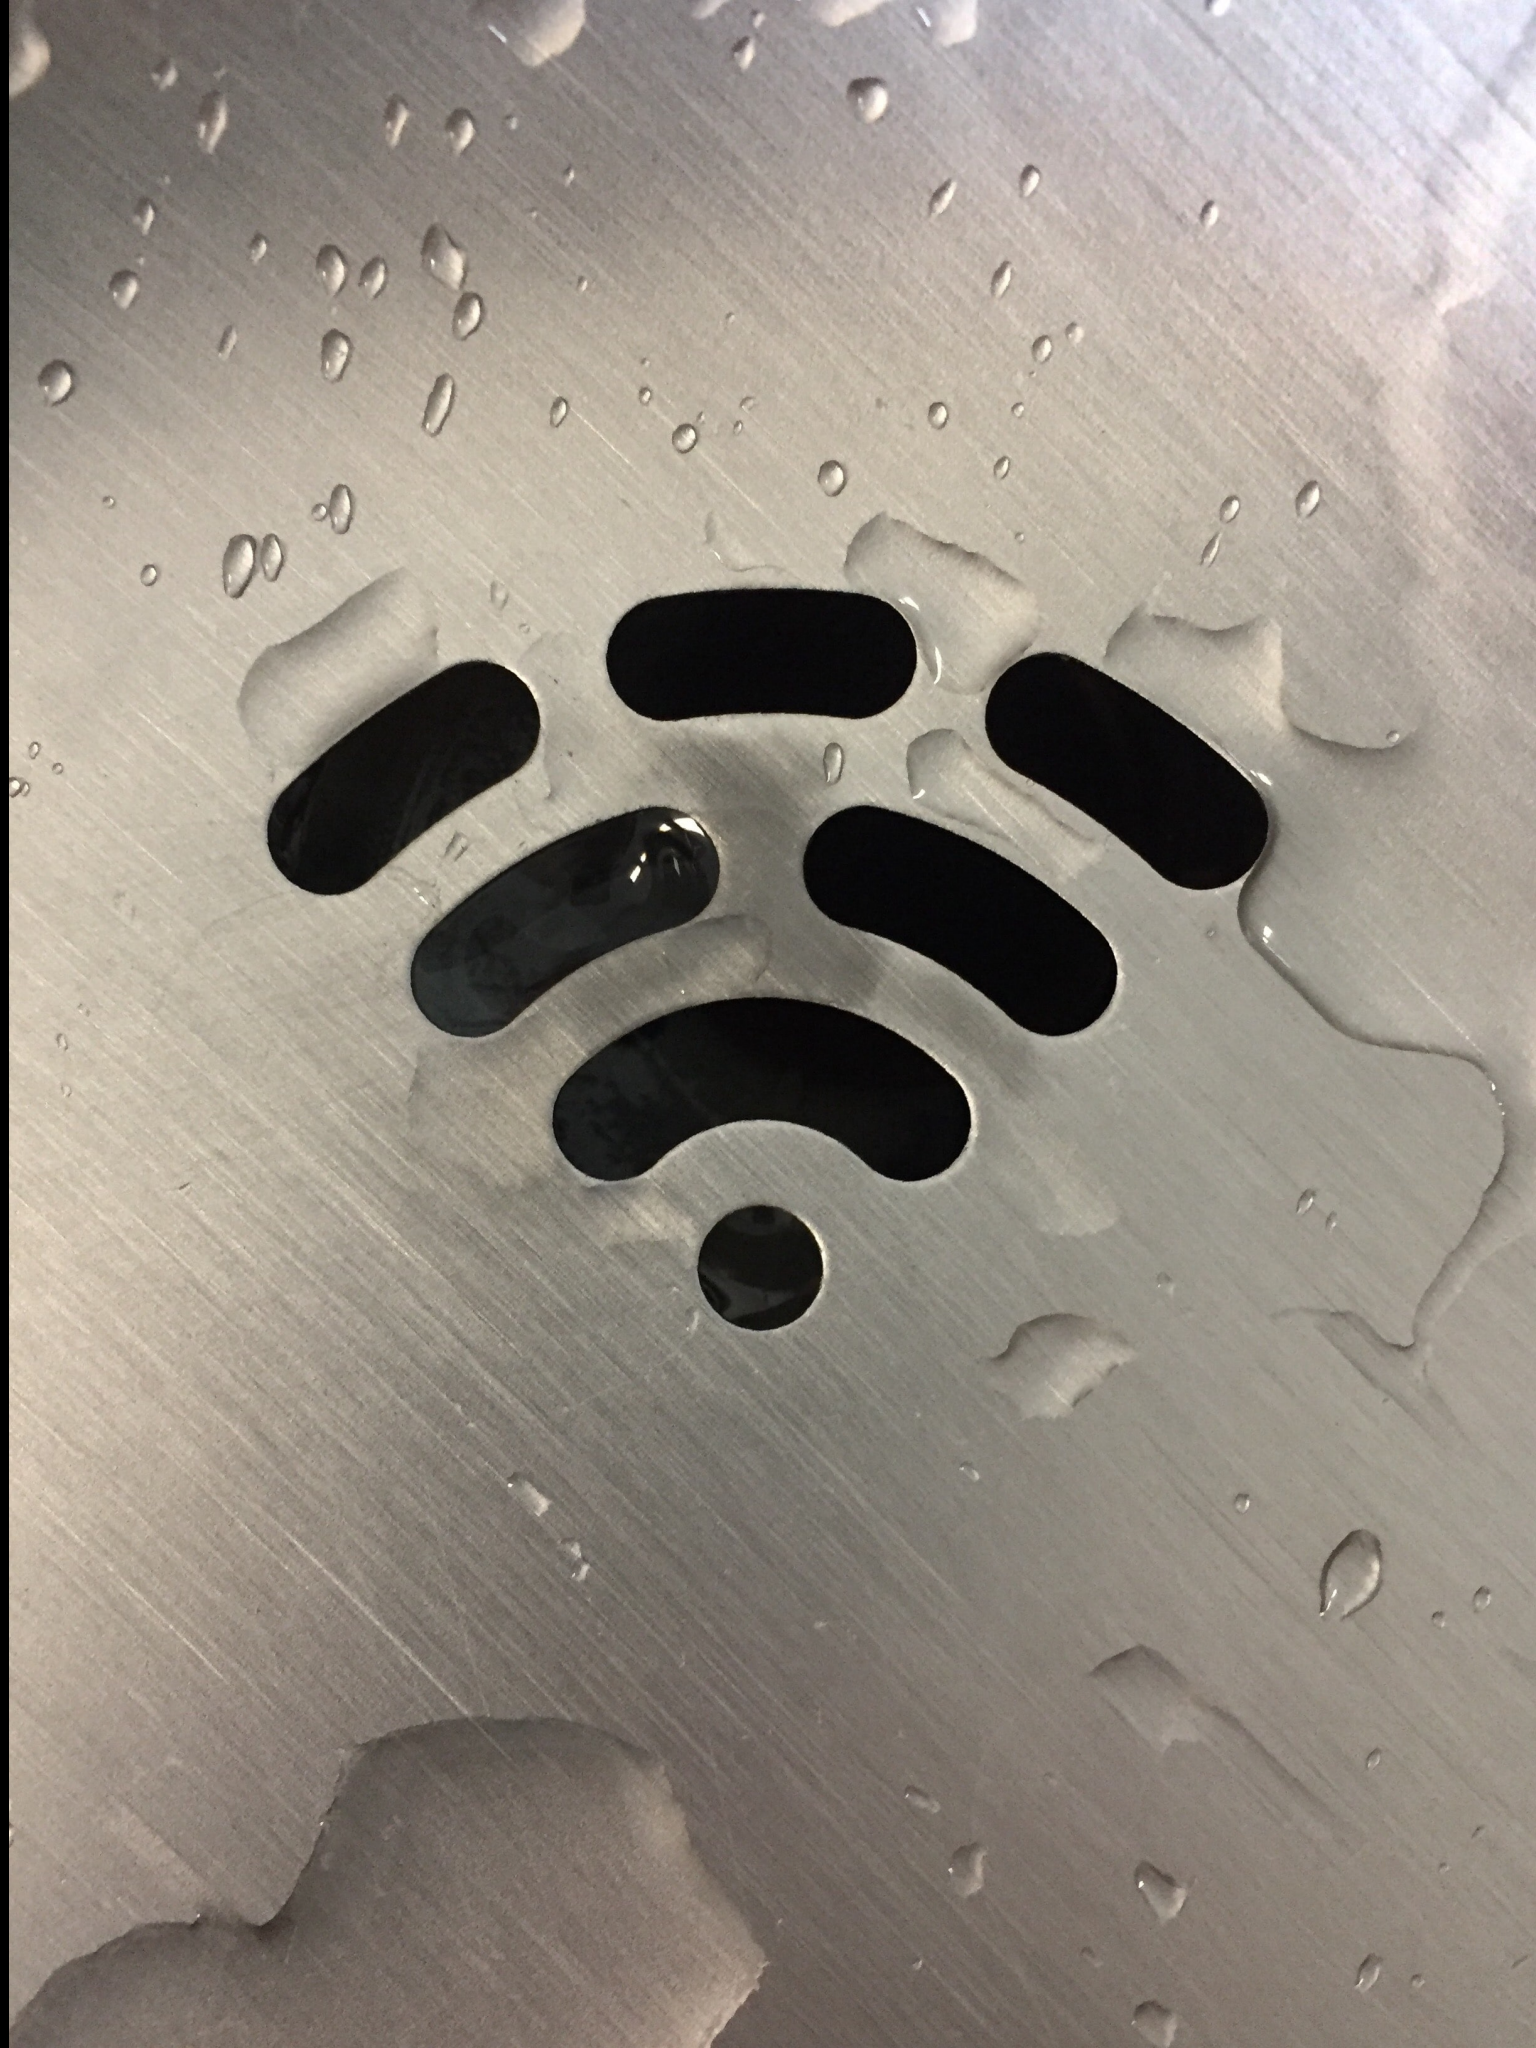

AGENDA

- Review Dashboard
- Past due
- Priority of the week
- Reimbursement PDF
- Issues/Risk Log
- Communications
- Q & A

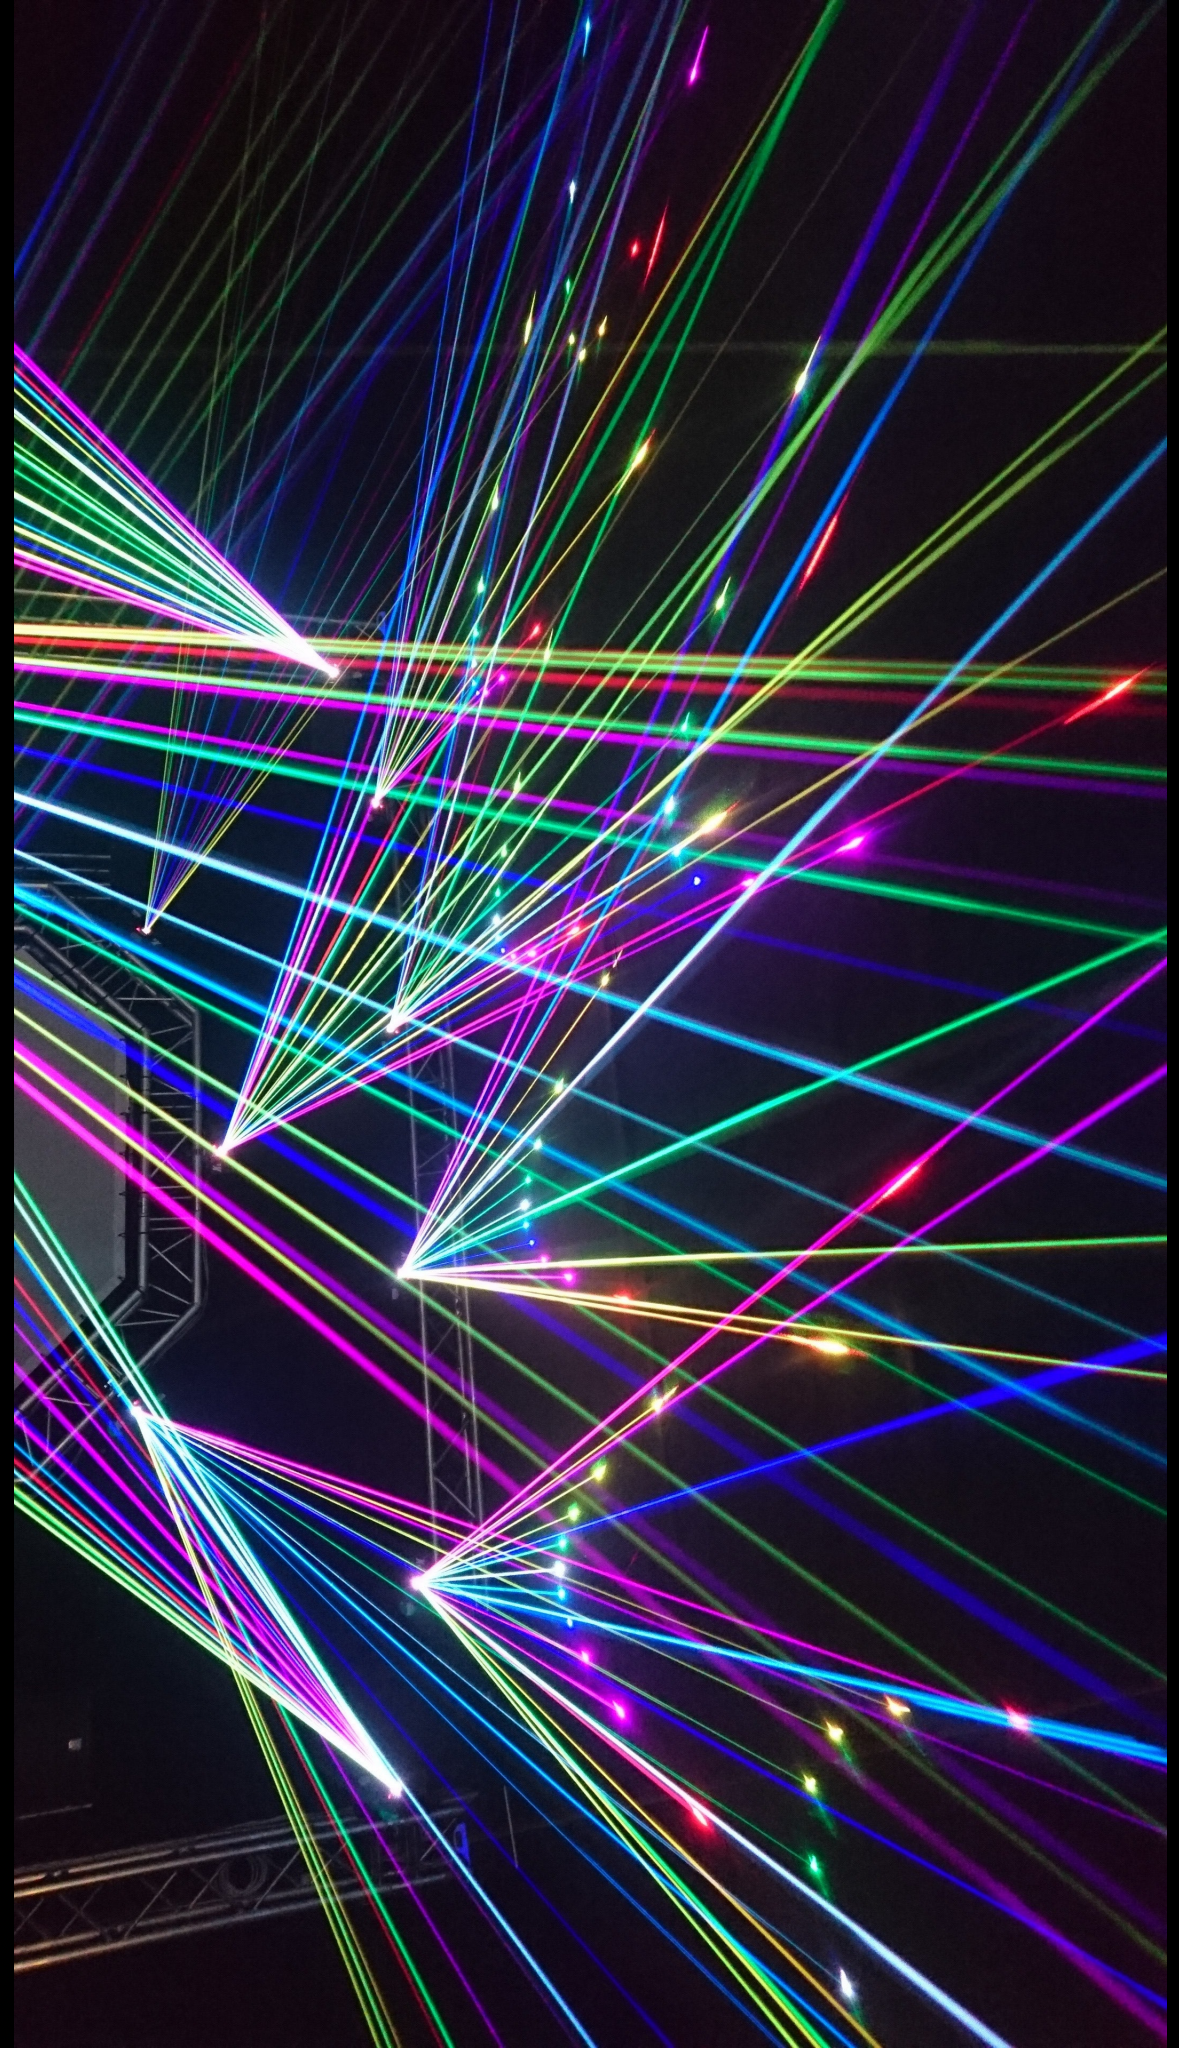













EQUIPMENT ORDERED

PAST DUE

- Who needs help?
- What can we do?

Equip. Ordered-Not compl... (8)

OVERDUE (8)

	Equipment Ordered	Jul 31
	In Progress	San Juan School Dist... 
	Equipment Ordered	Jul 31
	In Progress	Greenwood Charter Sch...
	Equipment Ordered	Jul 31
	New	Endeavor Hall
	Equipment Ordered	Jul 31
	In Progress	Garfield School Dist... 
	Equipment Ordered	Jul 31
	In Progress	John Hancock Charter Sc...
	Equipment Ordered	Jul 31
	In Progress	Tuacahn High School 
	Equipment Ordered	Jul 31
	In Progress	Lincoln Academy 
	Equipment Ordered	Jul 31
	In Progress	City Academy Charter Sc...













EQUIPMENT DELIVERED

PAST DUE

- Update status
 - Partial order in = In Progress
 - Complete order in = Completed
- Back ordered, how are you handling on these?
 - Make sure to submit a contact us ticket

Equip. Delivered - New (66)

OVERDUE (66)

 Equipment Delivered Aug 21 New Mountainville Academy
 Equipment Delivered Aug 21 New Millard School District
 Equipment Delivered Aug 21 New Excelsior Academy
 Equipment Delivered Aug 21 New Channing Hall
 Equipment Delivered Aug 21 New San Juan School District
 Equipment Delivered Aug 21 New Greenwood Charter School
 Equipment Delivered Aug 21 New Utah County Academy of Scie...
 Equipment Delivered Aug 21 New Merit Preparatory Academy
 Equipment Delivered Aug 21 New C.S. Lewis Academy
 Equipment Delivered Aug 21 New Bonneville Academy
 Equipment Delivered Aug 21 New Wasatch Charter School
 Equipment Delivered Aug 21 New Lakeview Academy

PROJECT DASHBOARD

16
WEEKS
LEFT!!!

Priorities this week - Equipment Delivered

Equip. Delivered - Compl... (25)	Equip. Delivered - In Prog... (42)	Equip. Delivered - New (66)
COMPLETED (25)	OVERDUE (42)	OVERDUE (66)
Equipment Delivered Aug 21 Completed Salt Lake School fo...	Equipment Delivered Aug 21 In Progress Entheos Academy Kear...	Equipment Delivered Aug 21 New Mountainville Academy
Equipment Delivered Aug 21 Completed Northeastern Utah...	Equipment Delivered Aug 21 In Progress Entheos Academy Mag...	Equipment Delivered Aug 21 New Millard School District
Equipment Delivered Aug 21 Completed Logan City School ...	Equipment Delivered Aug 21 In Progress Monticello Academy	Equipment Delivered Aug 21 New Excelsior Academy
Equipment Delivered Aug 21 Completed American Leaders...	Equipment Delivered Aug 21 In Progress Navigator Pointe Acad...	Equipment Delivered Aug 21 New Channing Hall
Equipment Delivered Aug 21 Completed Kane School District	Equipment Delivered Aug 21 In Progress Central Utah Educ...	Equipment Delivered Aug 21 New San Juan School District
Equipment Delivered Aug 21 Completed Salt Lake Arts Academy	Equipment Delivered Aug 21 In Progress Canyons School District	Equipment Delivered Aug 21 New Greenwood Charter School
Equipment Delivered Aug 21 Completed Wayne School District	Equipment Delivered Aug 21 In Progress Uintah School Dist...	Equipment Delivered Aug 21 New Utah County Academy of Scie...
Equipment Delivered Aug 21 Completed Vista School	Equipment Delivered Aug 21 In Progress Pinnacle Canyon Acade...	Equipment Delivered Aug 21 New Merit Preparatory Academy
Equipment Delivered Aug 21 Completed Roots Charter High Sch...	Equipment Delivered Aug 21 In Progress Jordan School District	Equipment Delivered Aug 21 New C.S. Lewis Academy
Equipment Delivered Aug 21 Completed Spectrum Academy	Equipment Delivered Aug 21 In Progress George Washingto...	Equipment Delivered Aug 21 New Bonneville Academy
Equipment Delivered Aug 21 Completed Soldeir Hollow Charter ...	Equipment Delivered Aug 21 In Progress Lincoln Academy	Equipment Delivered Aug 21 New Wasatch Charter School

PROJECT DASHBOARD

Priorities this week - Equipment Installed & Configured

16 WEEKS LEFT!!!

Equip Installed - Completed (4)	Equip Installed - In Progr... (11)	Equip Installed - New (114)
<p>+ Equipment Installed & C... Sep 4 Completed Soldeir Hollow Chart... 📄</p> <p>+ Equipment Installed & C... Sep 4 Completed Roots Charter High School</p> <p>+ Equipment Installed & C... Sep 4 Completed Northeastern Utah E... 📄</p> <p>+ Equipment Installed & C... Sep 4 Completed Salt Lake School for the ...</p>	<p>OVERDUE (10)</p> <p>+ Equipment Installed & ... Sep 4 In Progress Monticello Academy</p> <p>+ Equipment Installed & ... Sep 4 In Progress Sevier School District</p> <p>+ Equipment Installed & ... Sep 4 In Progress Jordan School District</p> <p>+ Equipment Installed & ... Sep 4 In Progress Washington County Sc...</p> <p>+ Equipment Installed & ... Sep 4 In Progress Gateway Preparatory A...</p> <p>+ Equipment Installed & ... Sep 4 In Progress American Preparatory ...</p> <p>+ Equipment Installed & ... Sep 4 In Progress Salt Lake City School Di...</p> <p>+ Equipment Installed & ... Sep 4 In Progress Ogden Preparatory Ac...</p> <p>+ Equipment Installed & ... Sep 4 In Progress Alpine School District</p> <p>+ Equipment Installed & ... Sep 4 In Progress Granite School District</p> <p>TODAY (1)</p>	<p>NEW (114)</p> <p>+ Equipment Installed & ... Sep 4 New Logan City School District</p> <p>+ Equipment Installed & ... Sep 4 New Mountainville Academy</p> <p>+ Equipment Installed & ... Sep 4 New Millard School District</p> <p>+ Equipment Installed & ... Sep 4 New Entheos Academy Kearns</p> <p>+ Equipment Installed & ... Sep 4 New Entheos Academy Magna</p> <p>+ Equipment Installed & ... Sep 4 New Excelsior Academy</p> <p>+ Equipment Installed & ... Sep 4 New Channing Hall</p> <p>+ Equipment Installed & ... Sep 4 New San Juan School District</p> <p>+ Equipment Installed & ... Sep 4 New Greenwood Charter School</p> <p>+ Equipment Installed & ... Sep 4 New Utah County Academy of Scie...</p> <p>+ Equipment Installed & ... Sep 4 New Merit Preparatory Academy</p>

Equipment Installed & Configured: Update status on subtasks

In Progress + Add assignee by Wrike B. on J

Aug 24 - Sep 4 (10d) Approvals 0:00 • 0:00 12 subtasks 3

<input checked="" type="checkbox"/>	Access Point(s) -Installed & Configured-Qty 100	Completed
<input checked="" type="checkbox"/>	Access Point(s) -Installed & Configured-Qty 100	Completed
<input checked="" type="checkbox"/>	Access Point(s) -Installed & Configured-Qty 100	Completed
<input type="checkbox"/>	Access Point(s) -Installed & Configured-Qty 100	New
<input type="checkbox"/>	Access Point(s) -Installed & Configured-Qty 100	New
<input type="checkbox"/>	Access Point(s) -Installed & Configured-Qty 1	New
<input type="checkbox"/>	Access Point(s) -Installed & Configured-Qty 1	New
<input type="checkbox"/>	Access Point(s) -Installed & Configured-Qty 1	New
<input type="checkbox"/>	Access Point(s) -Installed & Configured-Qty 1	New
<input type="checkbox"/>	Access Point(s) -Installed & Configured-Qty 1	New
<input type="checkbox"/>	Access Point(s) -Installed & Configured-Qty 10	New
<input type="checkbox"/>	Access Point(s) -Installed & Configured-Qty 10	New

K12 WIRELESS IMPROVEMENTS

COMMUNICATION

PROJECT WIKI

Find the FAQ, links, meeting presentations, meeting agenda.

The screenshot shows a web application interface for a project wiki. The top navigation bar includes the 'uen' logo, a menu icon, a red '+' button, 'Inbox', 'My to-do', a search bar, a help icon, and a user profile 'CS Country'. The left sidebar contains a 'Filter' section and a list of categories: 'Personal', 'Bookmarks', 'My to-do', 'Created by me', 'Shared with me' (with '-PROJECT WIKI' selected), 'A Training Project' (with 'Training Issues Log'), and 'Blueprints'. The main content area is titled 'Shared with me >' and '-PROJECT WIKI'. It features tabs for 'List', 'Board', 'Table', and 'Gantt Chart', with 'List' selected. Below the tabs are filters for 'All active tasks' and 'By Priority', along with a 'Leave feedback' link. The task list includes: 'Wrike Tip of the Day' (New), 'Weekly Agenda' (Dec 30, New), 'Announcements' (New), 'Weekly Meeting Presentations' (New), 'Links' (New), and 'FAQ' (New). Each task is preceded by a blue circle with a white plus sign and a person icon.

Task Name	Priority	Due Date	Status
Wrike Tip of the Day	By Priority		New
Weekly Agenda	By Priority	Dec 30	New
Announcements	By Priority		New
Weekly Meeting Presentations	By Priority		New
Links	By Priority		New
FAQ	By Priority		New

UEN.ORG - CARES ACT K12 WIRELESS IMPROVEMENTS

CARES Act K12 Wireless Improvements

 Meeting Videos


 Meeting Presentations

 FAQ


 Contact Us

Meeting Videos

8/19/2020

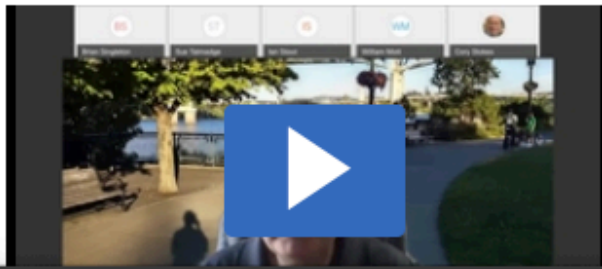


8/12/2020

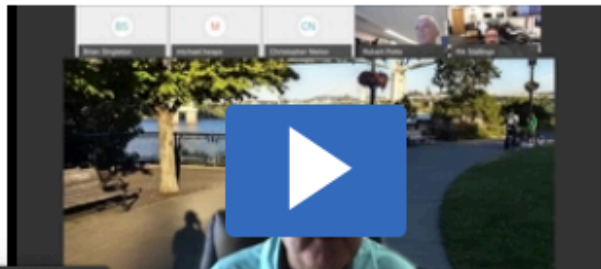

8/5/2020



7/23/2020



K12 WIRELESS IMPROVEMENTS

Q & A

